




Terminal 3 : Progress Update

5th February 2026



Current Status

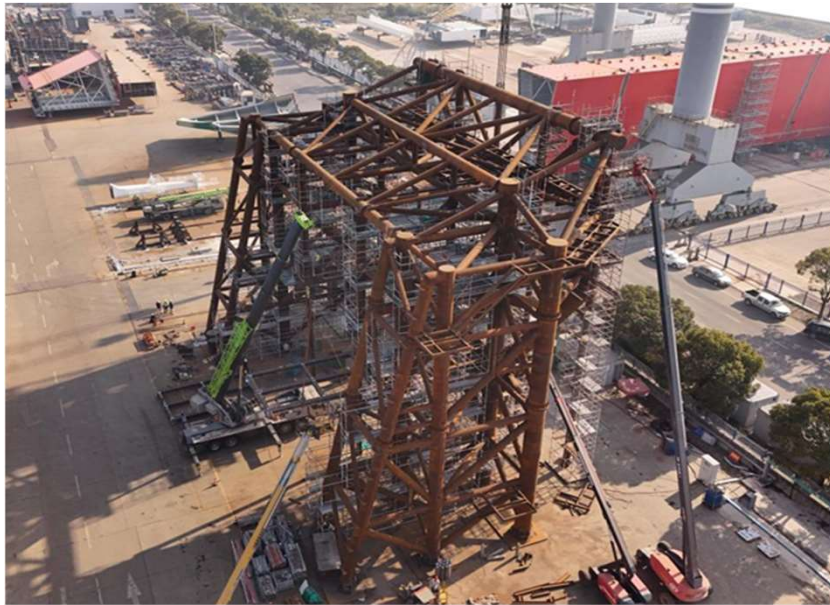
Construction Complete	30 th September 2026	
First Sailings	End of October 2026	
Project Cost	Within \$493m Budget	

Project Progress



Gantry

- On Program



- Trial assembly successfully completed
- Independent Quality Team based in China during construction (Bureau Veritas)



Gantry	Completion
Arrival (Devonport)	28 th January 2026
Off Load	18 th February 2026
Installation	22 nd May 2026



Marine Works

- On Program

Marine Works	Completion
Piling Works	Completed
Loading Ramp	1 st May 2026
Land Bollards	Completed
Guide Fender	26 th July 2026
Wharf Structures	14 th March 2026

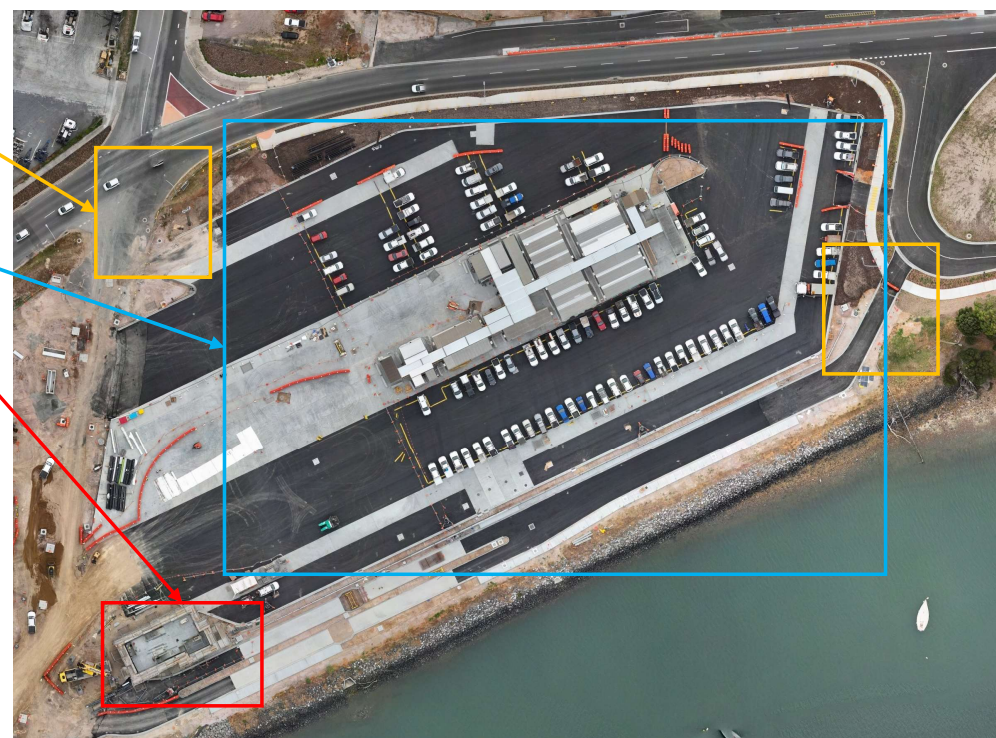
- Fender upgrade to C48 wharf by TasPort (April/May 2026)



Freight Yards

- On Program

Freight Yard	Completion
Freight Entrance	June 2026
Infrastructure	Completed
Asphalt	17 th February 2026
Buildings & Equipt.	30 th June 2026



BMD

FITZGERALD

GRADCO

Passenger Boarding

- On Program

Passenger Area	Completion
Entrance Road	29 th June 2026
Ticket Booths	27 th July 2026
Parking Lanes	15 th June 2026
Biosecurity	17 th July 2026

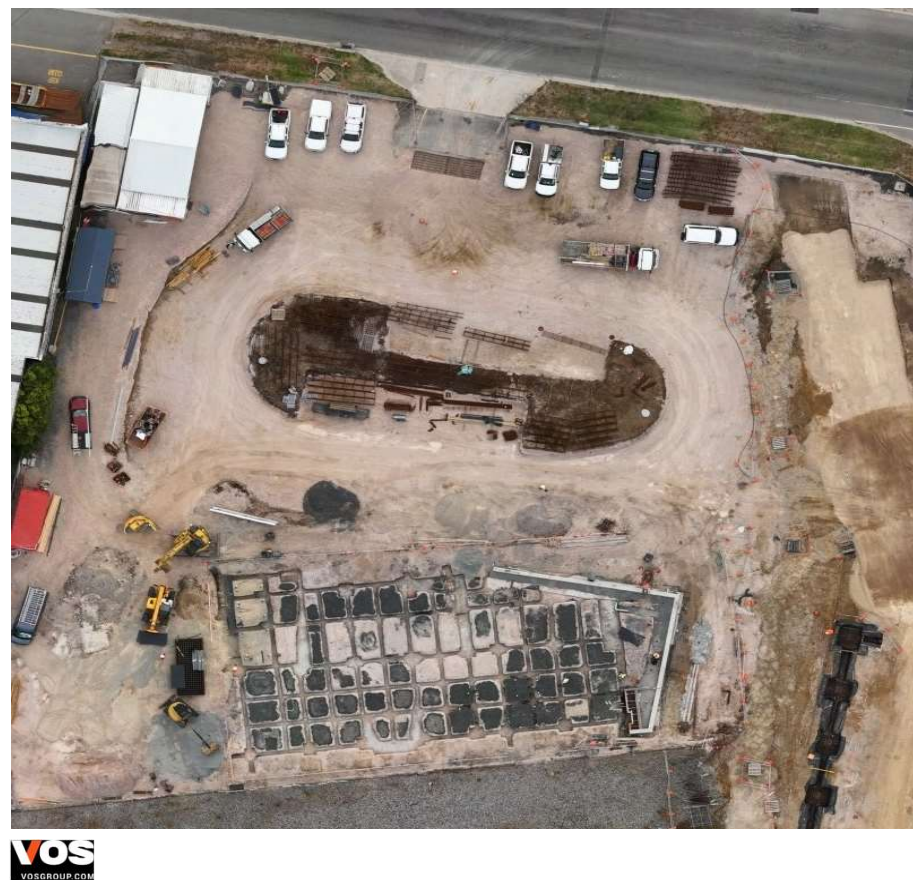
- Passenger lanes are required for gantry lay-down & assembly, construction will resume after gantry installation



Passenger Terminal







- On Program

Terminal	Completion
Foundations	Completed
Timber Frame	1 st May 2026
Weathertight	2 nd June 2026
Landscaping	30 th July 2026
Commissioning	30 th July 2026
Completion	30th August 2026



Commissioning

- Commissioning Activities

Work Area	July 2026	August 2026	September 2026	October 2026
Gantry & Linkspan				
Mooring Systems				
Freight & Passenger Areas				
Passenger Terminal				
Site Security & IT				
Integrated Testing				
Handover to Operations	
